

MODIS L1 Integration

12 August *19 August* 1999

Contents


- Summary Status
- Master Schedule
- Top Ten Issues

MODIS L1 Integration: Summary Status


12 August *19 August* 1999

- L1B (PGE2)
 - Version 2.1.6 in DAAC
 - Launch version is 2.2.1 **2.2.0** (deliver to DAAC on 16 Aug, promote to 5A ops by 20 **27**Aug)
- L1A and Geolocation (PGE1)
 - Promoted to DAAC ops (drop 4PY). Expect promotion ***promoted*** to 5A by 18 Aug
- Cloud Mask (PGE3)
 - Launch version in DAAC, promoting to 5A ops (expect 15 Sep: ***needs ECS 5A.01***)
- L1A Subsetter (PGE71)
 - Completed, delivered to DAAC, ECS delivered ESDT in 4PY.11. Promote to 5A ops by mid Sep
- L1B Subsetter (PGE 2A)
 - Launch version in DAAC, promoted to 4PY ops on 23 Jul. Expect promotion to 5A ops by 23 Aug
- Testing
 - Used L1B version 2.1.6 for MOSS 2
 - MOSS 2 completed
 - MOSS 3 planned for 28-30 Sep

MODIS LI Integration
MASTER SCHEDULE
19 August 1999

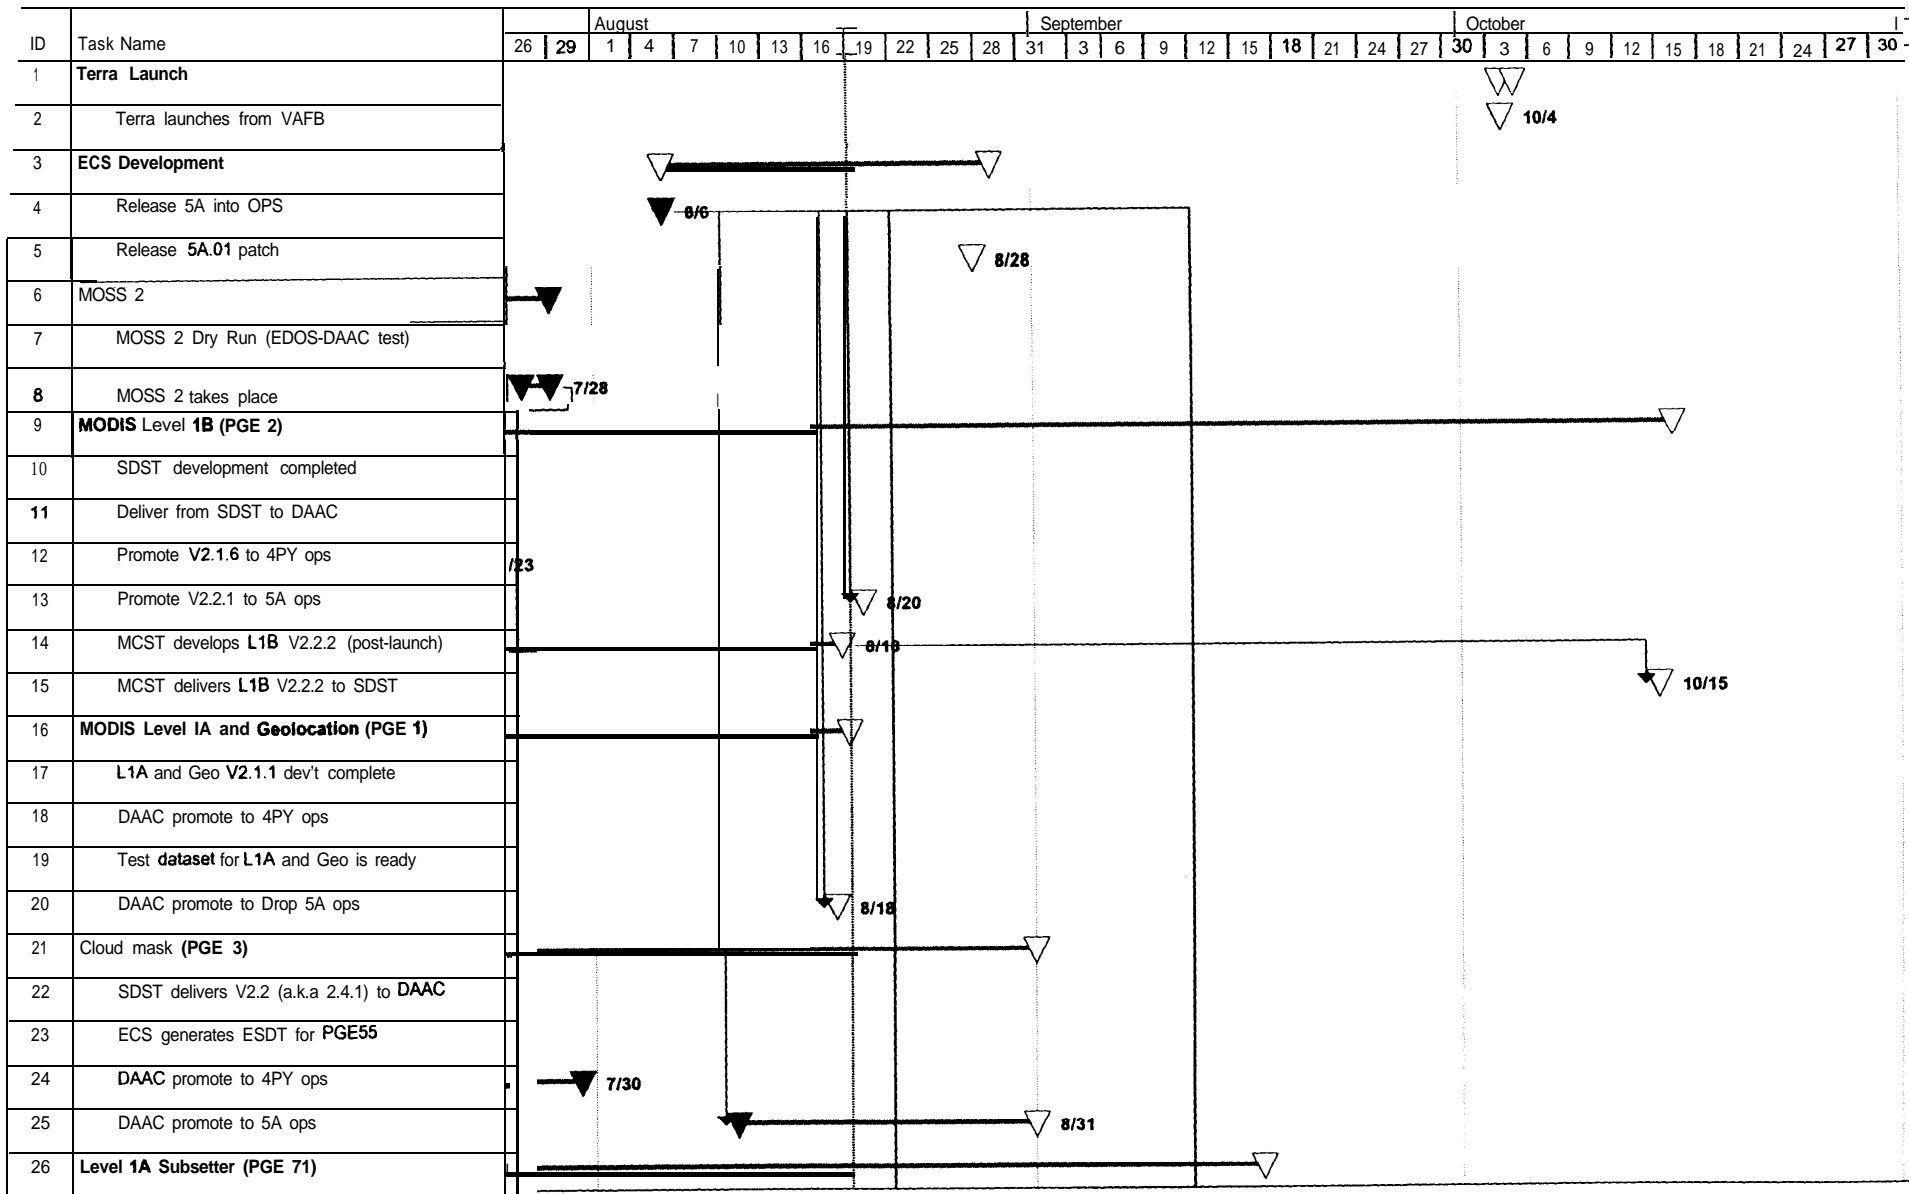

MODIS LI Integration
MASTER SCHEDULE
19 August 1999

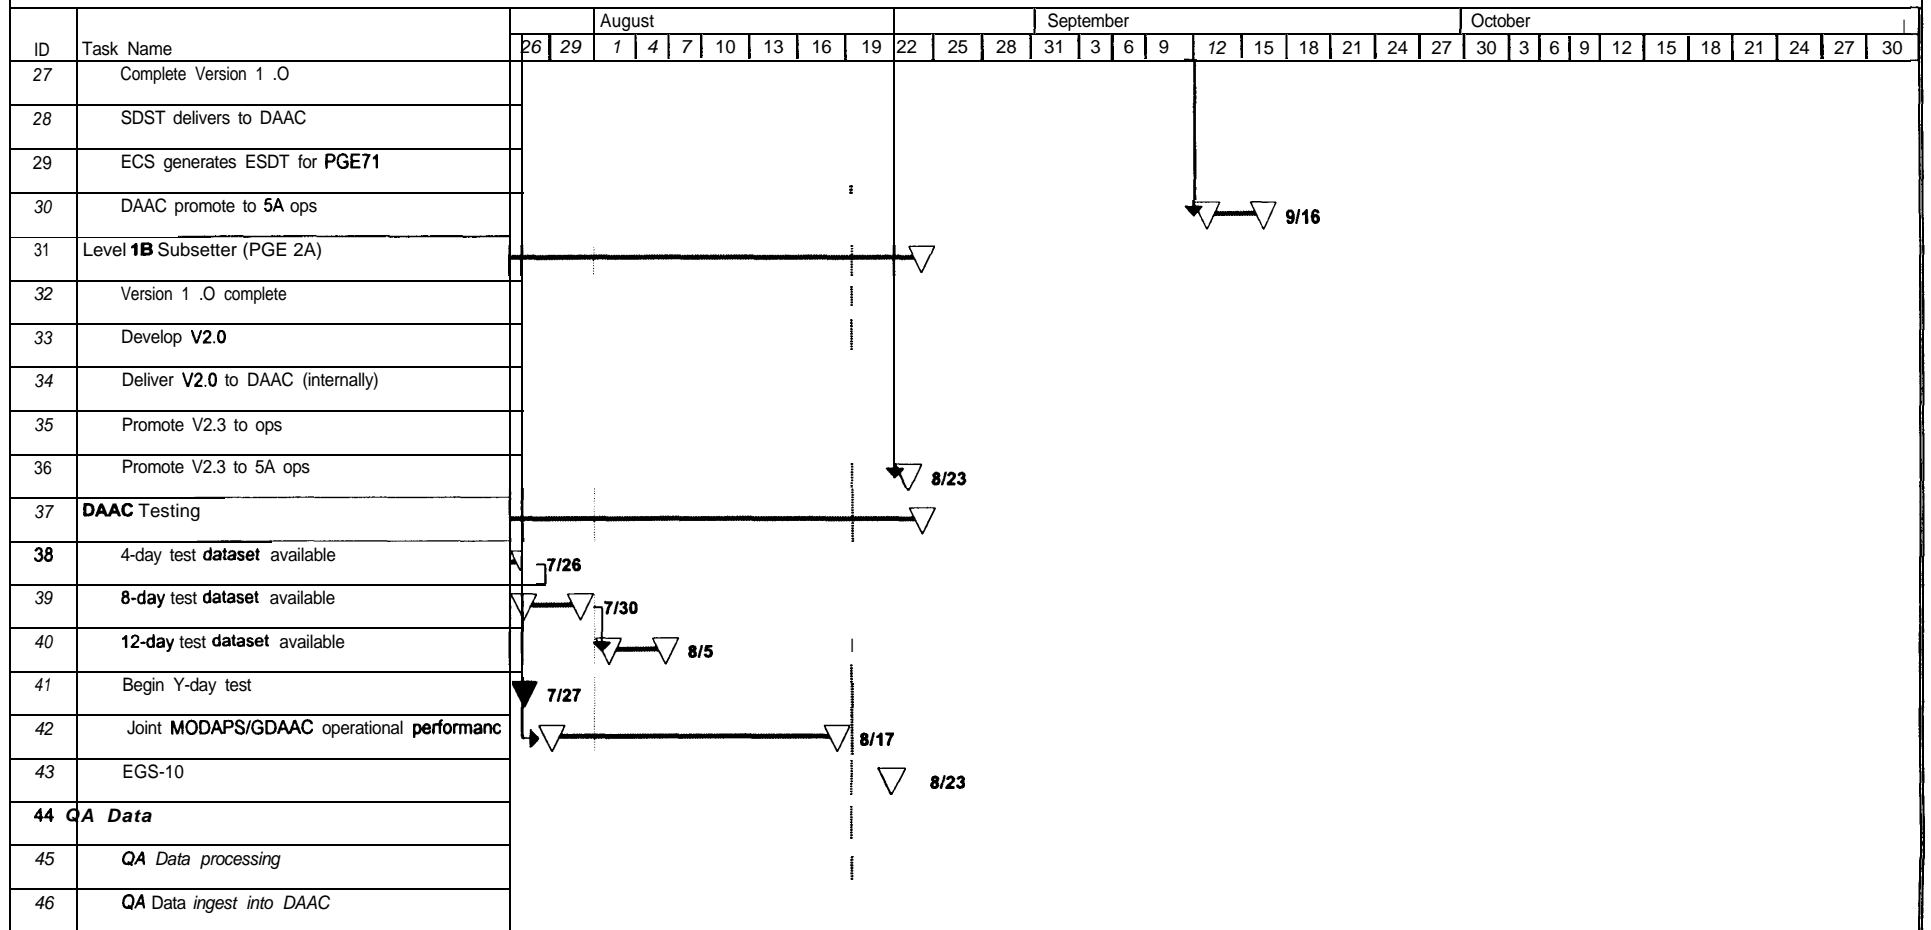

MODIS Level 1 Integration Issues

~~1942~~ August 1999

Item	Responsible Person	Due Date	Comments
<p>2.1. Find out what the schedule is for resolution of the following ECS problems at the GDAAC:</p> <ol style="list-style-type: none"> 1. Production plan fails when fractured data is received from EDOS. 2. Subscription Delivery Notice: User string not being filled in impacts cal/val of sensor. 3. Unable to delete Data Processing Requests (DPRs) 4. Autosys job boxes not completing. 	F Bordi	15 Jul 99	<p>The schedule for resolution of the four items listed is as follows:</p> <p>Item 2.1: End of August <u>– needs 5A.01 delivered 8/30</u></p> <p>Item 2.2: 15 September <u>– needs 5A.02 delivered 9/15</u></p> <p>Item 2.3: 15 September</p> <p>Item 2.4: this problem is expected to be fixed by the 5A.01 patch due at the end of August</p> <p>STATUS: OPEN</p>
<p>3.2. Decide which is the launch PGE: L1B 2.1.6 or 2.2.0</p>	RE Murphy	1 Jul 99	<p>REM will write memorandum articulating the difference between 2.1.6 and 2.2.0 and recommending which one is the launch version</p> <p>EM – SDST is comparing output products from L1B version 2.1.5 with L1B 2.2 output files. Both versions were run using L1A product made with the most current version of our synthetic data (Version 2.1.5). If the new L1B (V2.2) does not break the downstream processing (L2 and higher products) then we will want to put it in as the at-launch version of this PGE.</p> <p>REM decided that Launch PGE is 2.2.12.2.1 <u>2.2.0</u></p> <p>STATUS: CLOSED</p>
<p>4.3. Level 1 product data volumes are 94GB above the 2/96 baseline. The volume increases are as follows: 8GB in L1A, 1GB in geolocation fields and 85GB in L1B. Are we in agreement</p>	Ed Masuoka and Bob Murphy		<p>EM sent e-mail to the discipline leads discussing the problem.</p> <p>REM has convened a meeting of the discipline leads for Jul 29</p> <p>Discipline leads met on 29 Jul. REM to write report and recommendations</p>

that this will be handled by storing L1B for less than 6 months or is there another approach we should be pursuing?			EM to close out volumes and loads by end of August <u>(maybe sooner)</u>	
<u>5.4.</u> External data (GDAS)			<p>(MM) ESDIS has approved a CCR to support re-implementation of the ECS GDAS interface (NOAA changed the GRIB format without informing ESDIS of the change). ECS is in the process of re-implementing the interface, but the current development schedule does not have the changes completing until mid-July. We are looking for other resources to bring this date in but haven't found them yet.</p> <p>(MM) The fix for the GDAS format change has been integrated into the 4PY and 5A baselines and is being tested. It will be released as a patch by 7/30</p> <p>Delivery date to DAAC is 24 Aug 99 <u>30 Aug 99</u> as part of patch 5A.01</p> <p>STATUS: CLOSED <u>OPEN</u></p>	
<u>6.5.</u> DAAC support for PGE55			<p>(MM) We may need to update the DAAC processing requirements to support PGE55, since it is my understanding that this PGE will be executed in the DAAC to provide input to PGE03 sometime in the near post-launch timeframe. Although it is my understanding that the PGE does not have significant processing requirements, adding the requirements may help mitigate the risk identified under Item 7.</p> <p>(MM) We are adding support for PGE 55. We (ESDIS and ECS Science Office) need to work with the DAAC and MODIS to ensure that existing production rules are adequate. These changes should be reflected in an update to the MODIS Science Data Processing Software System Description and in the MODAPS SIPS ICD.</p> <p>MM will prepare written response by 20 Aug to close out this item</p>	
<u>7.6.</u> Establish policy and process to release L1 software to the public.	RE Murphy		STATUS: OPEN	
<u>8.7.</u> MCST is requesting ECS generate a	B Berriman		This new ESDT is a copy of the ECS core metadata into an ASCII file to support	

new ESDT for level 1B			<p>MCST daily QA activities. The method replicates QA activities already implemented at ECS by LDOPE</p> <p>(BG) Mike Linda is developing the L1B ESDT for QA. Expect submittal by 4 Aug</p> <p>The ESDT may already have been delivered. BGuenther and BVollmer to check by next meeting</p> <p><u>EM will hold CCB meeting</u></p> <p>STATUS: OPEN</p>	
11.8. From ETE-4, MCST received no Quick-look (EDS) data.			STATUS: CLOSED: expedited dataset was received in MOSS-2 <u>On 8/18</u>	
11.9. <u>Need to develop a versioning approach for the L1B product</u>	<u>B Guenther</u>			
